
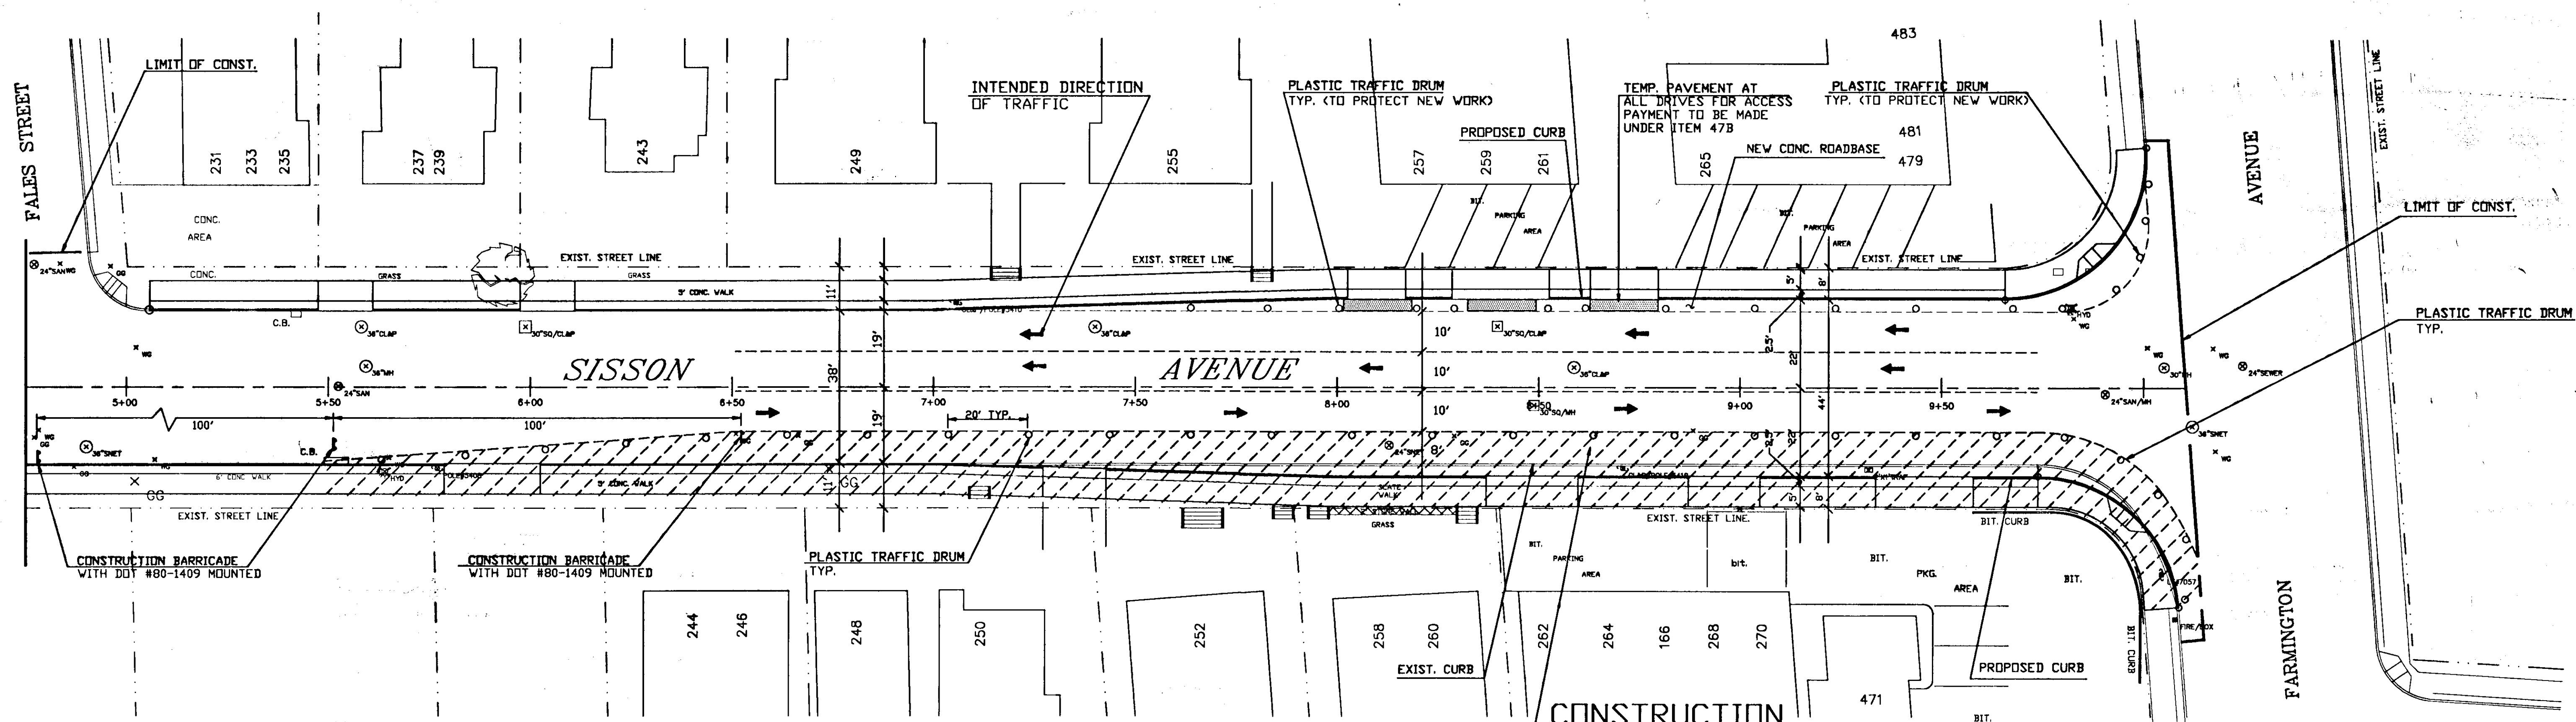


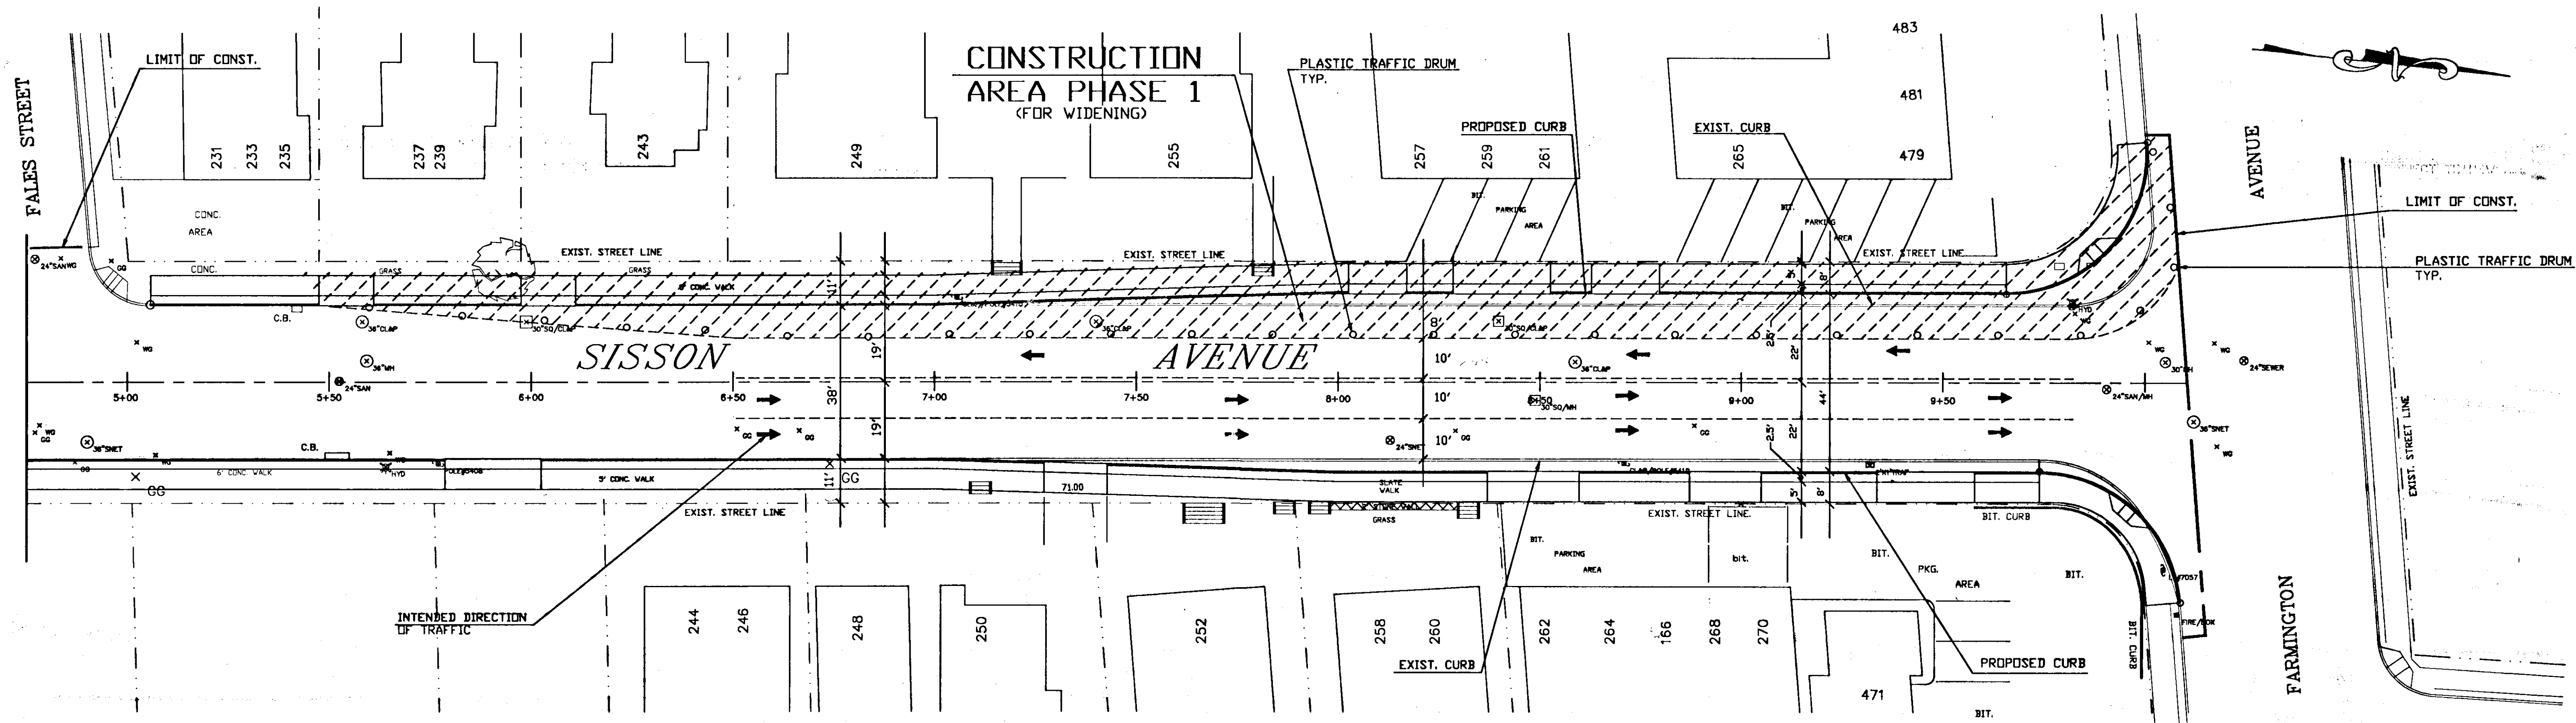

CONSTRUCTION PHASING NOTES

1. CONSTRUCTION FOR WIDENING IS TO BE LIMITED AND COMPLETED BY PHASE. ALL WORK WITHIN EACH PHASE (EXCEPT STRIPPING AND PAVING) SHALL BE COMPLETED IN ITS ENTIRETY PRIOR TO BEGINNING WORK IN A NEW PHASE.
2. STRIPPING/MILLING AND BIT, SHIM AND BASE COURSES SHALL BE COMPLETED ON ONE SIDE OF THE STREET AT A TIME. MAINTAIN ONE LANE OF TRAFFIC IN EACH DIR. DURING THESE OPERATIONS. FINAL PAVING SHALL BE COMPLETED AT NIGHT (7:00 PM TO 6:00 AM).
3. ALL SIGNAGE AND TRAFFIC CONTROL DEVICES ARE TO BE IN PLACE PRIOR TO ANY WORK BEGINNING.
4. THE CONTRACTOR IS REQUIRED TO MAINTAIN ALL TRAFFIC CONTROL DEVICES AND TO MAINTAIN A NEAT AND CLEAN CONSTRUCTION AREA TO THE SATISFACTION OF THE ENGINEER.
5. THE CITY RESERVES THE RIGHT TO CHANGE, MODIFY, OR LIMIT THESE PLANS IN THE INTEREST OF PUBLIC SAFETY.
6. ACCESS TO PRIVATE PROPERTIES AND BUSINESSES SHALL BE MAINTAINED AT ALL TIMES.

CONSTRUCTION AREA PHASE 2
(FOR WIDENING)

CONSTRUCTION OPERATIONS PER PHASE

1. INSTALL SIGNAGE, BARRICADES, DRUMS, AND ALL TRAFFIC CONTROL ITEMS.
2. REMOVE EXIST. WALKS, DRIVES, STAIRS, CURBING, ETC. AS INDICATED ON THE CONSTRUCTION PLAN.
3. CUT-BACK EXIST. SLOPES AND REGRADE AS REQUIRED.
4. RELOCATE/INSTALL NEW HANDHOLES, MANHOLE COVERS, CONTROLLERS, CATCH BASINS UNDERDRAIN, CONDUITS, PIPING, ETC.
5. CONSTRUCT NEW CURBING, WALKS, CONC. ROADBASE, STAIRS, RETAIN. WALL, ETC. AS REQUIRED.
6. TOPSOIL AND SOD ALL SLOPES AND DISTURBED GRASSED AREAS.
7. RELOCATE TO NEW PHASE UPON COMPLETION OF WORK.

CITY OF HARTFORD, CONNECTICUT DEPARTMENT OF PUBLIC WORKS ENGINEERING DIVISION		
RECONSTRUCTION AND WIDENING OF SISSON AVENUE CONSTRUCTION PHASING PLAN		
SHEET 11		
SUBMITTED	RECOMMENDED	APPROVED
PROJECT ENGINEER	DIVISION ENGINEER	CITY ENGINEER
DRAWN JLB	SCALE 1" = 20'	DAYBOOK NO. 011393
CHECKED DOT	DATE DEC. 1994	FILE NAME SISSON7.DWG
